

PROJECT UPDATE


August 2026



OVERALL PROGRESS LOOKING EAST



FRONT ENTRY AND GYM

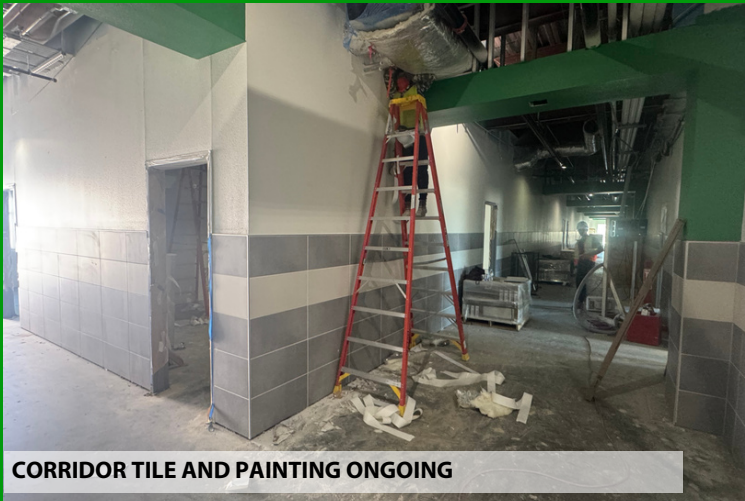

CORRIDOR TILE AND PAINTING ONGOING

CONSTRUCTION PROGRESS UPDATE

	Timeline	Project Progress
• Site work is ongoing	02/2027	61.5%
• Roofing is nearing completion	01/2027	
	12/2026	
• Brick veneer installation is 98% complete	11/2026	
	10/2026	
• Window installation is nearing completion	09/2026	
	08/2026	
• Sheetrock is ongoing throughout the building	07/2026	
	06/2026	
• Painting ongoing in classrooms and corridors	05/2026	
	04/2026	
• Tiling is ongoing	03/2026	
	02/2026	
• Ductwork is ongoing	01/2026	
• RTUs are installed and 80% wired	12/2025	
	11/2025	
• Permanent building power soon	10/2025	
	09/2025	
	08/2025	
	07/2025	
	06/2025	



MABANK ISD
MABANK ELEMENTARY SCHOOL 3/4



Designing Schools ... With Kids in Mind!

www.claycomb.net
